


Escuela Técnico Maya Design + Construction Update

October 11-24, 2010

#21

- Applied final layer of cob on Workshop 3 + 4.
- Laid gravel in Workshop 3.
- Transferred bodega into Workshop 3 and re-built temporary door.
- Workshop 2 ready to be transformed in to living space.
- Collected approximately 350 glass bottles. Cut, sorted, cleaned and made glass bricks. Experimented with foil and colored plastic.
- Designed and planned new detail for Workshop 3 + 4 end walls.
- Getting ready for patio roof.

1 cob finish; 2 gravel bodega floor; 3 temporary doors; 4 cutting bottles

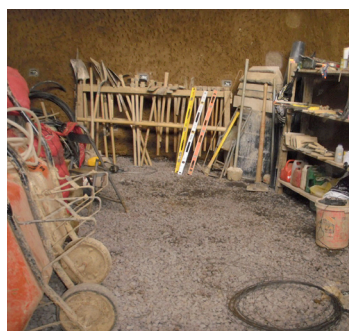

Plans for next two weeks . . .

- Pour concrete and terra-crete @ end walls
- Lay glass bricks @ end walls
- Finish forming West Bodega roof
- Erect patio roof
- Continue collecting glass bottles
